

MONTHLY PROGRESS REPORT

REPORT NO. 013 | June 2019

REPORT LISTING

Project Description	1
Project Information	1
Payment Status	2
Damages / Claims	2
Schedule Update	3
Construction Activity	3
Change Orders / PCOs	4
Issues / Concerns	4
Site Documentation	5 - 8
APPENDICES	
Payment Application	A-01
Three Week Look Ahead	N/A
Notable Correspondence	N/A

SOUTHBOROUGH PUBLIC SAFETY COMPLEX

SOUTHBOROUGH, MASSACHUSETTS



Pictures: Overall building progress

PROJECT DESCRIPTION:

This contract work is for a new Public Safety Complex Bldg. with Police and Fire Station headquarters. The station will include 5 apparatus bays, dispatch and communications, offices, dormitory space, kitchen, fitness room, and showers for the on-duty firefighters. The site is located right off of Cordaville Road and near Common Street. The new Police Station and Fire Station will be staffed 24 hours a day, 7 days a week.

The project was designed by Context Architecture (formerly Donham & Sweeney) of Boston, MA. CTA Construction Managers of Waltham, MA was selected as the General Contractor. Both CTA Construction Managers and the Town of Southborough ("Town") executed a Standard Form of Agreement between Owner and Contractor (AIA A101). The Agreement stipulated sums of \$15,125,000.00 for complete construction.

PROJECT COMPLETION

LAST REPORT

80%*

*as of Pay App No. 12

CURRENT REPORT

88%**

**as of Pay App No. 13

PROJECT INFORMATION:

Owner:
 Town of Southborough
 17 Common St.
 Southborough, MA 01772
 508.480.0161

Owner's Project Manager:
 The Vertex Companies, Inc. ("VERTEX")
 Kevin Heffernan
 400 Libbey Parkway
 Weymouth, MA 02189
 781.952.6000 / 6060F

Architect:
 Context Architecture ("Context")
 Jeff Shaw
 98 Harrison Ave
 Boston, MA 02111
 617.423.1400

Contractor:
 CTA Construction Managers ("CTA")
 Jared Dougan, PM
 400 Totten Pond Road
 Waltham, MA 02451
 781.786.6624

PAYMENT DETAILS

PAY APP NO. 13

Date Executed by Contractor
July 1, 2019

Date Certified by Architect
July 7, 2019 (est.)

Original Contract Amount
\$15,125,000.00

Approved Change Orders
\$ 1,059,644.08

Amended Contract Amount
\$ 16,184,644.08

Approved To Date
\$14,303,827.88

Retainage Withholdings
\$715,191.43

Paid To Date
\$12,311,819.37

Pending Payment
\$1,276,817.08

Remaining To Bill
\$2,596,007.63

PAYMENT STATUS

A schedule of values ("SOV") was initially provided by CTA Construction Managers to the Owner, Context and Vertex for review. The SOV is an outline of the project cost break-downs per trade. The SOV will have adjustments as the rest of the sub-contractors get on board, there were no comments at this time, but continues to get reviewed at the weekly project meetings.

Payment Application No.1 was submitted for payment on July 6, 2018 in the amount of \$454,843.85

Payment Application No.2 was submitted for payment on August 6, 2018 in the amount of \$439,691.91

Payment Application No.3 was submitted for payment on September 11, 2018 in the amount of \$602,151.54

Payment Application No.4 was submitted for payment on October 9, 2018 in the amount of \$979,857.02

Payment Application No.5 was submitted for payment on November 6, 2018 in the amount of \$1,071,930.46

Payment Application No.6 was submitted by CTA on November 29, 2018 for the building committee to approve in the amount of \$804,796.65

Payment Application No. 7 was submitted by CTA on December 31, 2018 for Vertex and Context to review in the amount of \$812,053.12. Comments were issued to CTA, and the application was revised to \$797,993.72.

Payment Application No. 8 was submitted by CTA on January 25, 2019 for Vertex and Context to review in the amount of \$1,293,845.02. The revised application was \$1,266,788.94.

Payment Application No.9 was submitted by CTA on February 26, 2019 for Vertex and Context to review in the amount of \$1,753,556.09. The revised application was \$1,638,302.96.

Payment Application No.10 was submitted by CTA on March 27, 2019 for Vertex and Context to review in the amount of \$1,789,5859.16. The revised application value was \$1,710,201.66.

Payment Application No. 11 was submitted by CTA on April 30, 2019 for Vertex and Context to review in the amount of \$1,296,845.92. The revised application value was \$1,254,275.61.

Payment Application No. 12 was submitted by CTA on May 24, 2019 for Vertex and Context to review in the amount of \$1,464,326.75. The revised application value was \$1,290,685.14.

Payment Application No. 13 was submitted by CTA on July 1, 2019 after review by Vertex and Context in the amount of \$1,276,817.08. The application did not need to be revised.

PROJECT COMPLETION

LAST REPORT

80%*

*as of Pay App No.12

CURRENT REPORT

88%**

**as of Pay App No. 13

POTENTIAL DAMAGES

There are no potential damages to report at this time.

AFFIRMATIVE CLAIMS

There are no affirmative claims at this time.

SCHEDULE UPDATE

The Town, Vertex, and Conext discussed the schedule in great detail over the past month. It was determined that a new substantial completion date will now be August 13, 2019. Part of this agreement was that CTA provide an updated schedule weekly (every Friday before the close of business). CTA has continued to provide the updates to date; and the latest schedule from 06.28.19, indicates no set-backs at this time.

CONSTRUCTION ACTIVITY

Site:

Site work is on-going. Paving is scheduled for the beginning of July. Once completed, that will leave curbing, landscaping, final paving and line-striping to finish with site work.

Electrical:

Permanent power has been delivered by N-grid. The electrician is schedule to "liven-up" the building by the middle of July. Rough-in work for the entire building is approximately 90%, Finishes are approximately 80% on the interior. Exterior finishes will likely start at the end of July.

Exterior Work:

Asphalt will be placed the first week of July. Carport Steel is scheduled for the first week of July.

Steel:

Car port steel is scheduled to be installed early next month.


Plumbing , HVAC, and Interior Work:

Plumbing finishes are approximately 90% complete, HVAC finishes are approximately 90% complete. Town vendors (dispatch furniture, E-911, WB Mason, Motorola) are scheduled throughout next month.

Safety:

CTA Construction Managers along with VERTEX have been ensuring on-site job safety.

Average Daily Workforce

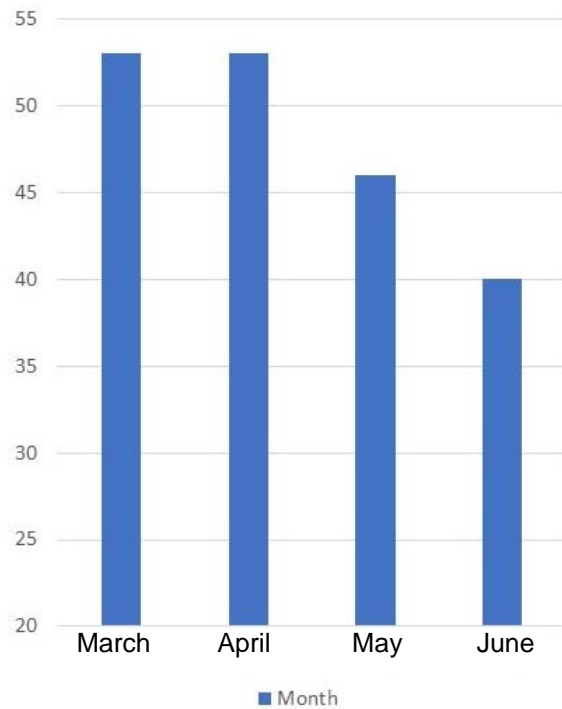

Workforce:

The average daily workforce has been approximately 40 workers per day. The low for the month was 5 workers (on a Saturday), the high was 53 workers.

Certified Payrolls:

Certified payrolls continue coming in to Vertex from the sub-contractors. VERTEX will maintain copies, and review all certified pay-rolls.

CHANGE ORDERS / PROPOSAL REQUESTS

PCO No.	CE No.	CCD No.	Description	Total
1	1		Seismic clips (ASI 02) - (\$8,025.67)	\$ -
2	2	1	Clubhouse trailer upgrades & storage containers	\$ 8,926.12
3	3		Cleanouts (ASI 01) (original value - \$2,070.09)	\$ 1,447.38
4	4		Guardrail curbing & asphalt (RFI 01) (\$3,927.00)	\$ 1,309.37
5	5		Kitchen Sink Revision (RFI 10) - Orig. \$7,429.42 - Revised	\$ 1,173.19
6	6		Ice maker - plumbing connection (RFI 15/ASI 05) (\$1,550.79)	\$ -
7	8		Clubhouse dampproofing - (\$2,580.52)	\$ -
8	10	2	Clubhouse foundation revisions	\$ -
9	11		Clubhouse HVAC - (\$4,417.58)	\$ -
10	12	3	Clubhouse plumbing (10,564.85)	\$ 6,137.27
11	13	4	Clubhouse basement ceiling demo	\$ 3,969.24
12	14	6	Temp clubhouse electrical	\$ 6,631.02
13	15	5	Clubhouse electrical demo (\$5,040.33)	\$ 3,000.00
14	16		Ice maker - electrical	\$ 645.15
15	17		Plumbing permit fees (\$2,395.31)	\$ -
16	18		Sewer pump electrical revisions (\$24,225.38)	\$ 17,301.24
17	19		Not yet received	
18	20		Clubhouse temporary power	\$ 20,752.67
19	21		Clubhouse deck / ramp revisions (\$15,524.77)	\$ 1,380.06
20	22		Clubhouse duct demolition	\$ 881.84
21	23		Clubhouse ADA paving	\$ 8,886.24
22	24	RFI 27	Clubhouse foundation drainage	\$ 3,708.21
23	25	RFI 36	Moisture mitigation	\$ (20,000.00)
24	26		Brick alternate	\$ (43,000.00)
25			Glass & glazing revisions	\$ 14,979.06
26		9	Ledge removal (orig. \$10,000 - superceded by PCO 42)	\$ -
27	31	RFI 24	Clubhouse mixing valve	\$ 2,750.48
28			Locker room Misc mirrors	\$ 2,051.18
29			Water line size revision	\$ (4,967.15)
30			Elevator floor	\$ (161.79)
31			Not yet received	
32			Plumbing fixture P-17	\$ 11,807.60
33			Clubhouse interior stairs	\$ 5,937.34
34			Shower revisions	\$ 28,695.14
35			Misc. metals revisions	
36			Hydrant and FD connection	\$ 5,688.00
37			Pass through window	\$ 11,231.62
38			Clubhouse trailer & storage containers	\$ 3,167.10
39			Not yet received	
40			Clubhouse gas line credit	\$ (1,220.16)
41			Detention glazing	\$ 3,431.23
42			Ledge removal	\$ 44,520.00
43			Fire alerting system	\$ 107,340.51
44			Clubhouse revisions	\$ 25,964.00
45			N line steel support at masonry	\$ 2,315.36
46			Training tower revisions	\$ (1,220.07)
47			SEE BID SAVINGS DETAIL BELOW	
48			Flow meter	\$ 6,804.94
49			Fire rated glazing	\$ 1,423.77
50			Clubhouse electrical submeter	\$ 1,803.73
51			Antenna bracket revisions	\$ 1,483.28
52			Not yet received	
53			Phase 1 & 2 time extension	\$ -
54			Lobby floor insignias	\$ 6,567.76
55			Electrical panel revisions	
56			Credit for handicapped rail	\$ (2,459.59)
57			Not yet received	
58			Not yet received	
59			Cornice revisions	\$ 16,658.22
60			Clubhouse trench drain & piping	\$ 11,567.82
61			Epoxy floors	\$ 80,611.26
62			Metal roof edge	\$ 3,314.45
63			Turnout gear lockers	\$ 32,951.20
64			LED signs	\$ 7,854.00
65			Not yet received	
66			Not yet received	
67			Dimple door frame	\$ 841.50
68			Detention hardware revisions	\$ (1,950.24)

69			Appliance revisions	\$ 246.83
70			Misc GWB framing revisions	
71			Electrical revisions	\$ 4,844.91
72			Brick supports at corners	\$ 4,844.24
73			Electronic keying at detention	\$ 1,486.77
74			Chair rail revisions	\$ (411.06)
75			Eliminate gas to dryers	\$ (3,765.45)
76			Not yet received	
77			Decon shower pan	\$ 2,179.91
78			Not yet received	
79			Not yet received	
80			Doors C202 & C206 stair revisions	
81			Septic tank core size conflict	\$ 785.40
82			Grease skimmer (\$19,342.20)	\$ -
83			Clubhouse revisions	\$ 14,624.06
84			Drain line extension	\$ 2,117.56
85			Relieving angle at stair tower	\$ 9,837.85
86			Security revisions	\$ 6,181.52
87			Not yet received	
88			Not yet received	
89			Elevator penthouse damper	\$ 4,999.99
90			Not yet received	
91			Steel kicker	\$ 3,134.00
92			Waterline revision	\$ 1,133.70
93			Not yet received	
94			Kitchen hood controls	\$ 538.56
95			Not yet received	
96			Dayroom TV wall	\$ 723.64
97			Not yet received	
98			Framing at entry roof knee wall	\$ 2,153.53
99			Interior window sealant	\$ 13,285.85
100			Not yet received	
101			Tight tank drainage	\$ 6,426.54
102			Booking window	\$ 4,480.82
103			Electrical revisions - 2nd floor	\$ 2,119.02
104			Not yet received	
105			Not yet received	
106			Room 210 windows (\$3,671.54)	\$ -
107			Elevator damper crane remobilization	\$ 2,226.41
108			Not yet received	
109			Training tower relieving angle masonry	\$ 1,577.87
110			Added air supply outlet	\$ 3,115.05
111			Plumbing vent relocation	\$ 2,170.30
112			Not yet received	
113			Not yet received	
114			Not yet received	
115			Not yet received	
116			Added trees	\$ 8,796.43
117			Tight tank 40' extension	\$ 5,688.54
118			Not yet received	
119			Shower framing revisions	\$ 4,381.86
120			Kitchen sink	\$ 4,344.59
121			Floor insignia	\$ 579.63
TBD	TBD	7	Power for Golf cart chargers at relocated Clubhouse	\$ 4,000.00
Totals				\$ 571,779.42
BID SAVINGS BREAKDOWN				
PCO No.	CE No.	CCD No.	Description	Total
47			Parking canopies	\$ 350,609.69
Totals				\$ 350,609.69

ISSUES / CONCERNS

1. At the time of this report, Vertex's main concern is getting permanent power on in the building, as it could potentially have an impact on the schedule.

SITE DOCUMENTATION

01



Photo depicts the progress of the exterior of the front of the building.

02



Photo depicts the exterior progress on the west end of the building.

03



Photo depicts the progress of the exterior of the rear of the building.

04



Photo depicts exterior progress around main entrance

SITE DOCUMENTATION

05



Photo depicts the progress of the booking area

06



Photo depicts the finished/protected flooring on the second floor.

07



Photo depicts the progress of restrooms throughout building

08



Photo depicts the progress of the lobby floor.

SITE DOCUMENTATION

09



Photo depicts the progress of the apparatus bay floor

10



Photo depicts the progress of the kitchen

11



Photo depicts the progress of the fitness room floor

12

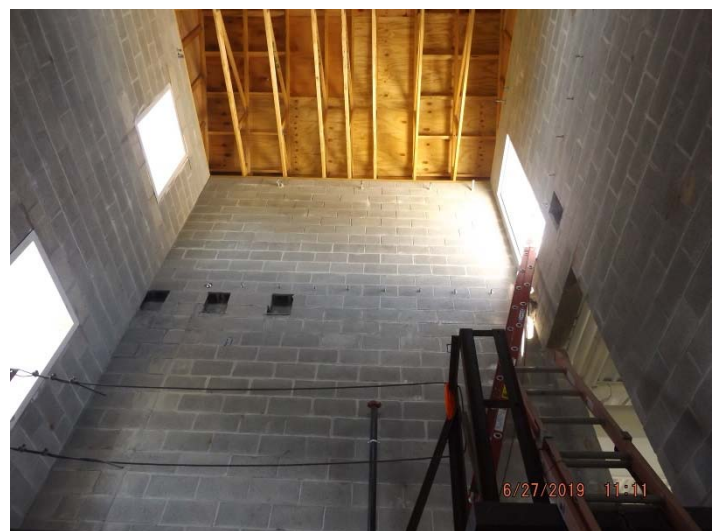


Photo depicts the progress of the training tower

SITE DOCUMENTATION

13



Photo depicts the progress of asphalt

14



Photo depicts the progress of asphalt

15



Photo depicts the progress of asphalt, and footings ready for carport steel

16



Photo depicts the completion of the elevator damper.



Appendix A-01

APPLICATION FOR PAYMENT NO. 13
(cover page only)

APPLICATION AND CERTIFICATE FOR PAYMENT

AIA DOCUMENT G702

PAGE ONE OF

PAGES

TO THE OWNER: Name: **Town of Southborough**
 Address: **17 Common Street**
Southborough, MA 01772

PROJECT: Name: **Southborough Public Safety**
 Address: **32 Cordaville Road**
Southborough, MA 01772

APPLICATION NO.: **13**
 PERIOD TO: **06/30/19**
 APPLIC DATE: **06/30/19**

Distribution to:
 OWNER
 ARCHITECT
 CONTRACTOR

FROM CONTRACTOR: **CTA Construction Managers, LLC**
 400 Totten Pond Road 2nd Floor
 Waltham, MA 02451

VIA ARCHITECT: Name: **Context Architecture, Inc.**
 Address: **68 Harrison Avenue**
Boston, MA 02111

CONTRACT DATE:

CONTRACT FOR: Southborough Public Safety

CONTRACTOR'S APPLICATION FOR PAYMENT

Application is made for payment, as shown below, in connection with the Contract

Continuation sheet, AIA document G703, is attached.

1. ORIGINAL CONTRACT SUM	\$	<u>\$15,125,000.00</u>
2. Net change by Change Orders	\$	<u>\$1,059,644.08</u>
3. CONTRACT SUM TO DATE (Line 1 + or - 2)	\$	<u>\$16,184,644.08</u>
4. TOTAL COMPLETED & STORED TO DATE (Column G on G703)	\$	<u>\$14,303,827.88</u>
5. RETAINAGE:		
a. 5% % of Completed Work	\$	<u>\$715,191.43</u>
(Columns D + E + F on G703)		
b. % of Stored Material	\$	<u></u>
(Column on G703)		
Total Retainage (Line 5a + 5b or Total in Column 1 of G703)	\$	<u>\$715,191.43</u>
6. TOTAL EARNED LESS RETAINAGE (Line 4 less Line 5 Total)	\$	<u>\$13,588,636.45</u>
7. LESS PREVIOUS CERTIFICATES FOR PAYMENT (Line 6 from prior Certificate) (amount paid to date)	\$	<u>\$12,311,819.37</u>
8. CURRENT PAYMENT DUE	\$	<u>\$1,276,817.08</u>
9. BALANCE TO FINISH, INCLUDING RETAINAGE (Line 3 less Line 6)	\$	<u>\$2,596,008</u>

CHANGE ORDER SUMMARY	CO's	CCD's
Total changes approved in previous months by Owner	\$896,888.63	\$94,550.59
Total approved this Month	\$68,204.86	\$0.00
TOTALS	\$965,093.49	\$94,550.59
NET CHANGES by Change Order & CCD's	\$1,059,644.08	

The undersigned Contractor certifies that to the best of the Contractor's knowledge, information and belief the Work covered by this Application for Payment has been completed

in accordance with the Contract Documents, that all amounts have been paid by the

Contractor for Work for which previous Certificates for Payment were issued and payments received from the Owner and that current payment shown herein is now due.

CONTRACTOR: CTA Construction Managers, LLC

By: _____ Date: _____

State of: MASSACHUSETTS

County of: MIDDLESEX

Subscribed and sworn to before
me this _____ day of _____

Notary Public:

My Commission expires: _____

ARCHITECT'S CERTIFICATE FOR PAYMENT

In accordance with the Contract Documents, based on on-site observations and the data comprising this application, the Architect certifies to the Owner that to the best of the Architect's knowledge, information and belief the Work has progressed as indicated, the quality of the Work is in accordance with the Contract Documents, and the Contractor is entitled to payment of the AMOUNT CERTIFIED.

AMOUNT CERTIFIED \$ _____

(Attach explanation if amount certified differs from the amount applied for. Initial all figures on this Application and on the Continuation Sheet that are changed to conform to the amount certified.)

ARCHITECT **Context Architecture, Inc.**

By: _____ Date: _____

This Certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the Contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or Contractor under this Contract.
